



Quotation

Drop In Wicket



Cost Breakdown

Drop In Wicket

Supplied, Delivered & Installed

Supply & install 1 Gabba Drop in synthetic wicket 11 x 2.4m wide x 2.0 long custom concrete panels.

Finished slab of 22m long x 2.4m wide.

Supply & install 1 Gabba Grass portable synthetic wicket 22m x 2.4m

The Turf area 22.2m x 2.6m x 50mm deep is to be cut out, levelled & prepared by school.

Lifting slings supplied for future installations & removals.

Portable stumps with flat base are to be used

Note: As for preparation a small amount of topsoil is removed to allow for the panels to be installed (approx. 80mm) deep x the width and length of the wicket. Each panel is about 800kg providing good body to the bounce and play of the wicket with the Gabba Grass surface rolled out over the levelled concrete.

A standard permanent wicket is 100mm in thickness vs drop-in wicket 60mm

Total Price Excluding GST

\$45,995.00



Terms & Conditions

Payment terms: 50% deposit on purchase order, 25% on supply of materials on site and final 25% payment on completion and sign off.

Excludes: Council requirements (DA & BA) – Ex Gabba works.

CONDITIONS OF QUOTATION:

1. Please note that specifics of the quotation including prices and quantities are subject to confirmation prior to commencement of any work. Prices quoted cover only services nominated.
2. This quotation remains valid for 30 days from the quotation date.
3. If our quotation is accepted, work will be undertaken by employees of Gabba Sporting Products and /or our nominated sub-contractors.
4. The conditions of offer are shown in our quotation and our offer does not imply our willingness to enter into a sub-contract agreement containing conditions that differ from our offer.
5. All variations to contract must be made in writing, signed and approved by an authorised representative prior to additional work commencing.
6. Gabba Sporting Products has built its name on quality products & workmanship, all care will be taken whilst working on site. We do not accept any responsibility for any damage to buildings, services or surrounding landscapes as we will be working in conjunction with the property engineers & stakeholders.
7. It is the client's responsibility to mark out boundaries and/or have the boundary surveyed, and services such as Phone, Power, Water & Gas must be located by the client.
8. To facilitate vehicle and machine entry to the site, a suitable path is to be nominated by the client. The client is to provide ground protection mats in place if the path is soft & likely to be damaged.
9. Unless otherwise specified, quotations are based on standard soil conditions for excavation. In the event of rock, hard fill or foreign material being encountered, further costs as required for excavation / earthwork will be applied.
10. This quote is subject to site inspection. If the work site is found to contain unforeseen obstacles, resulting in need for additional earthwork, structural support etc., this quote will no longer be valid and a new quote will be issued.
11. All soil lifted during excavation will be moved within the grounds, no soil will be removed from the property, a suitable location will be arranged with the grounds staff prior to excavation work starting.
12. Whilst every effort is made to complete the works within a timely manner, deviation from the anticipated time frame may be encountered in unfavourable weather conditions or where unforeseen obstacles are encountered within the site.
13. Site specific inductions that exceed thirty (30) minutes in length will incur a charge based on our hourly rate.
14. In the event of a dispute, the client agrees to provide details of the dispute in writing within 7 days of receipt of our invoice. If no details are provided within this time, all due monies are to be paid as per our agreed trading terms.
15. Notwithstanding the Terms & Conditions outlined above, these terms will not negate any state or federal regulation in any way.
16. It is the customer's responsibility to ensure sufficient access, equipment, and personnel are available to unload the entire order from the truck.

Accepting the above works, items, notes & payment terms



Full Name: _____ Signature: _____ Date: _____

Kind Regards Mitch Gaskell





Premium Cricket Facility Solutions

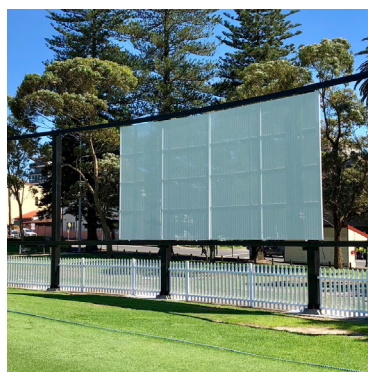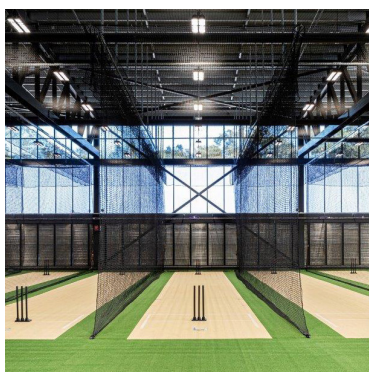

Premium Netting & Synthetic Grass

- Braided High Density Polyethylene Netting
- UV-treated
- Tensioned & spring-loaded options
- Roped edges
- TEST 10mm & 12mm non-directional synthetic grass
- Green, Hybrid, Blue & Black colour options

Structural Posts & Footings

- Engineer-certified footings
- Australian-made structural steel
- Hot-dip galvanised or black finish

● Soft Netting Options ●

● Turf Block System (Side-Folding) ●

● Retractable Netting & Storage Tidy Boxes ●

● Post-less Systems ●

● Indoor Multi Sports Courts ●

● Indoor Training Lanes ●

● Cricket Sight-Screens ●

More information available online

